




AIRPORT WAY / CUSHMAN STREET INTERSECTION RECONSTRUCTION

PROJECT NO. 0002312 / Z640780000

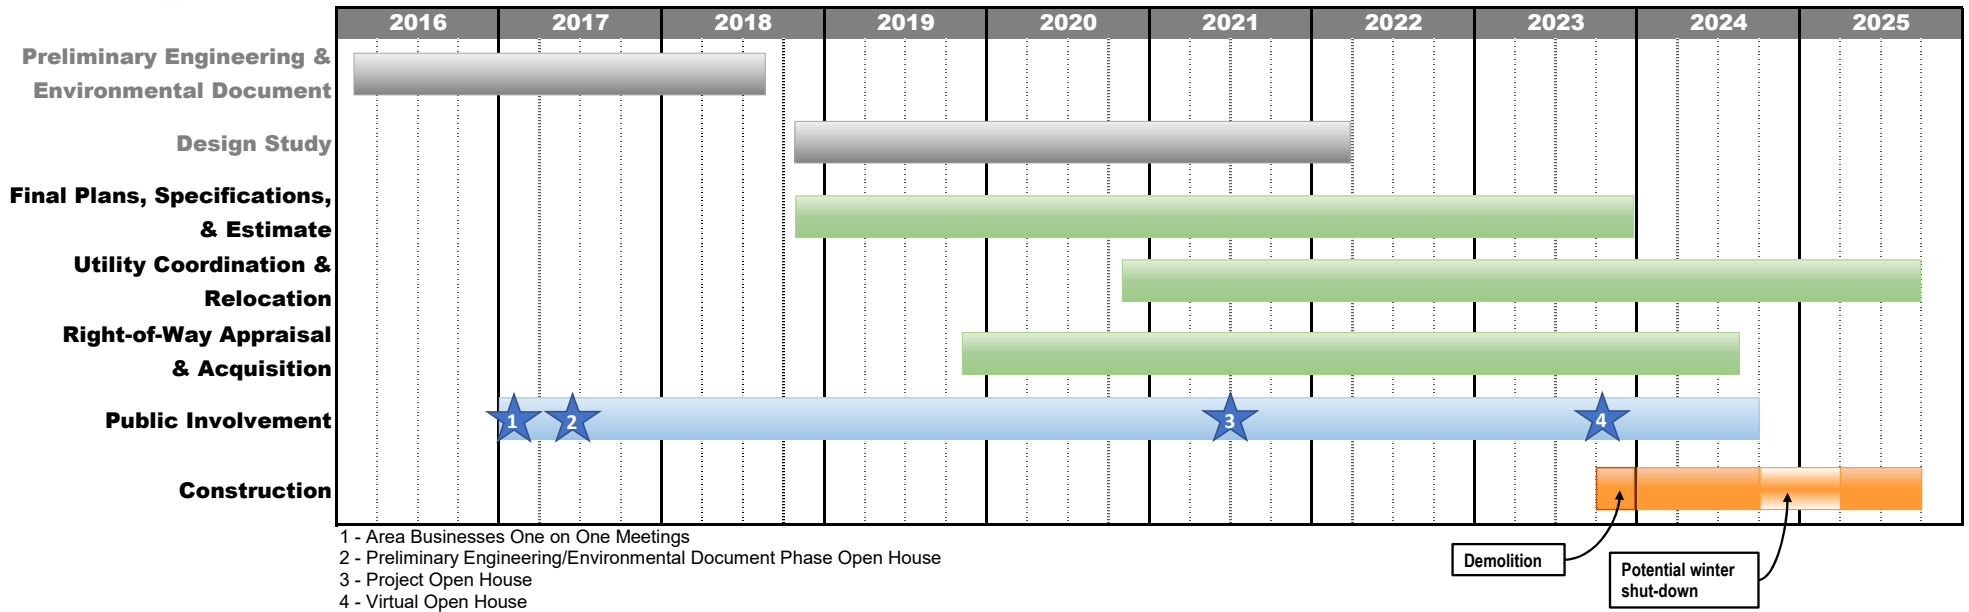

What Has Been Done?

- A Traffic Safety Analysis Report was completed in November 2016 to evaluate existing traffic operations, pedestrian and motorist.
- One-on-One Meetings were held with area businesses in February 2017 to discuss the project and its impacts to properties.
- The Preliminary Engineering & Environmental Document Phase was completed in July 2018.
- The Design Study was finalized and signed in Spring 2022.
- HC Contractors was selected as the contractor for CMGC delivery in Spring/Summer 2022.
- The project was approved by FNSB local planning authority in July 2022.
- The 95% plans, specifications, and estimate were completed in December 2022.

What's Next?

- The project is currently funded through Construction.
- Final Plans, Specifications, and Estimate are scheduled to be completed by December 2023.
- Utility Coordination began in November 2020. Utility Relocations are anticipated to begin in late summer 2023 and continue through the 2025 construction season.
- Right-of-Way Appraisal & Acquisition certification is estimated to be completed by Summer 2024.
- Construction related to demolition and utility relocations are currently programmed to begin in Fall 2023 and will continue through 2025 along with the roadway construction.
- Public Involvement will be ongoing through design and construction.
